Irish Water

Leakage Reduction Programme

First Fix Leak Repair Scheme

For Domestic Water Customers

Quarterly Report

Q2 2018






1. Introduction to the Leakage Reduction Programme¹

Water is one of our most valuable resources. Clean potable water is expensive to produce and distribute and one of Irish Water's key priorities is to reduce the level of water wasted through leakage. Irish Water produces 1.7 billion litres of treated water every day. Some 600 million litres (35%) per day is utilised by domestic households; 300 million litres (18%) per day is provided to non-domestic operation and the remaining 800 million litres (47%) is lost through leaking pipes. Almost half of the clean water we produce is lost through leakages.

In October 2015, Irish Water announced a €5.5 billion investment to improve drinking water quality and wastewater infrastructure up to 2021. This plan will see the investment in water conservation and network improvement initiatives double to €512m in the period 2017 to 2021 through the implementation of a targeted programme of works, called the *Leakage Reduction Programme*.

The overall aim of these works is to reduce leakage on a national scale to economically sustainable levels, leading to improved water network performance and reliability. The Leakage Reduction Programme and associated works will ensure a clean, safe and reliable public water supply now and into the future to support our growing population and economy.

For this programme, Irish Water has sub-divided the country into eight regions and is working in partnership with local authorities and regional contractors to plan and complete activities. Details of the Leakage Reduction Programme regions and contractors can be seen below.

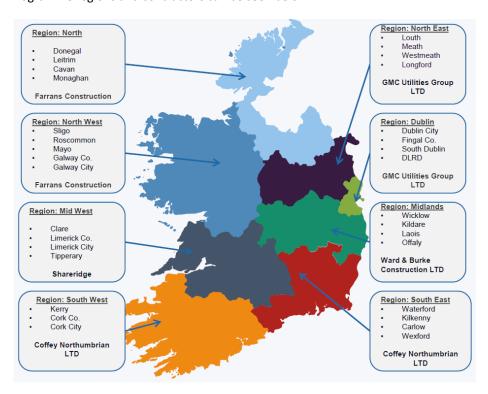

¹ Following the completion of the Metering Programme in Q1 2017, the First Fix Leak Repair scheme moved to become part of the wider national Leakage Reduction Programme.



The scope of the works included in the Leakage Reduction Programme (LRP) includes undertaking improvements under the following seven principal work streams;

1. DMA (District Metering Area) Establishment

This involves the identification of groups of premises and the installation of a district meter to monitor water usage. This identifies works needed within the DMA to ensure efficient operations.

2. Find & Fix

The Find & Fix scheme involves leak detection crews undertaking surveys using sounding equipment to locate leaks on pavements and other public areas. If a public side leak is identified, Irish Water will carry out the necessary repairs.

3. First Fix Free

The First Fix Free scheme offers free leak investigations and free repairs for qualifying properties where a constant flow of water is found on the external water supply pipe. Irish Water estimates that nearly 129 million litres of water per day have been saved as a result of this scheme to the end of Q2 2018. Further information on the First Fix Free scheme can be found at https://www.water.ie/water-supply/first-fix/.

4. Mains Renewal including Shared & Backyard Services

Water mains renewal works usually include the replacement or renewal of ageing public water mains to improve water quality and supply. As our water pipes are underground, we need to dig down to inspect the pipes and carry out any necessary repairs or replacements.

A shared service connection means that two or more properties are fed by a single water pipe. These connections pipes are often made of iron or lead and prone to leaks.

In some older properties water connections may be installed to the back of the property and run through customer's back gardens. These connections are prone to leaks and can cause reduced levels of service and poor water pressure.

5. Lead Services

Lead in drinking water is a recognised health concern. We will be investigating the pipes that connect individual properties to the public water mains and replacing any lead pipes with new plastic pipes.

6. Non-Domestic Metering

Irish Water is replacing old non-domestic meters installed by the Local Authorities with new meters that have Automatic Meter Reading technology. The new meters allow for more accurate and timely billing for customers and better identification of leakage on non-domestic customer sites.

7. Pressure Management

Pressure management works are required to improve the quality and security of water supply to customers. The aim of these works is to reduce leakage within the mains network and to ensure a consistent supply of water to all customers. Too much pressure in the network can result in burst pipes and leakage. This can then result in a low water supply pressure for customers at the tap.



2. Overview of First Fix Free Scheme

In May 2014 the Government announced funding of €51m for a scheme to address water leakage on pipework within customer properties under a "First Fix" scheme². Following a public consultation in August 2015 the Commission for Regulation of Utilities (CRU) approved Irish Water's proposed First Fix Leak Repair Scheme. The First Fix Leak Repair scheme was mobilised under the national Domestic Metering Programme.

Under the First Fix Leak Repair scheme, Irish Water assists customers by notifying them where suspected leakage is occurring within the boundary of their property. Leaks which are identified on the external supply pipe serving a property are offered a free leak repair. The First Fix Leak Repair scheme does not apply to leaks within a dwelling.

Utilising meter read data to identify the most significant leaks has proven key to operating the First Fix Leak Repair scheme efficiently. Prior to the introduction of the First Fix Leak Repair scheme, leakage programmes had been based around time-consuming and labour intensive sampling of areas in order to seek to detect anomalies on pipework. The Irish Water domestic metering programme has provided both the platform and the technology based solution to address this challenge. Data obtained from meter reading information highlights unusual water usage patterns and allows Irish Water to isolate the source of leaks to a particular property, thereby reducing the time required for leak investigation.

Given the need to prioritise water conservation, Irish Water prioritises repairs under the First Fix Leak Repair scheme by size, based on the volume of water lost. A constant flow of water, (that is 6 litres per hour over a 48 hour period), will trigger a constant flow alarm (CFA) on the meter, indicating a potential leak. The largest leaks wasting the most water are priorities to be fixed first.

It is estimated that nearly 129 million litres of water per day is being saved as a result of First Fix repairs completed under the Metering Programme and Leakage Reduction Programme.

3. How to avail of the scheme

Customers can avail of the scheme, once they are aware of a leak on their property. The CFA alarm is triggered where a constant flow of water to the property is identified (6 litres per hour over a 48 hour period). When a CFA alarm is recorded, customers are issued with a letter from Irish Water, indicating a potential leak on their property.

Customers with a visible leak on their property can also contact Irish Water to avail of a free leak investigation. Following the findings of the Joint Oireachtas Committee in 2017, Irish Water is engaging with the CRU in 2018 to assess how the benefits of the First Fix policy can be further applied to leaks on the customer side of unmetered properties.

² As outlined in section 8 of this report, IW is currently working within this original revenue allowance.



4. Initiatives to increase Customer Engagement Levels

Following the completion of the First Fix Scheme under the Metering Programme in February 2017, Irish Water analysed engagement levels in order to establish initiatives to improve the First Fix process and increase productivity.

The First Fix scheme is relying on the following in order to achieve water reduction;

- The First Fix letter reaching its desired destination to inform the customer of the possible leak.
- The customer engaging with Irish Water in order to arrange a leak investigation.
- The customer returning the signed waiver allowing Irish Water to repair the leak on their property.

The following initiatives have been implemented:

First Fix Letter

In an attempt to increase performance of the scheme, Irish water pursued the following initiatives:

- In Quarter 2, Irish Water sent 16,456 First Fix letters to properties with a constant flow alarm. Letters were issued to properties with a constant flow alarm plus usage in excess of 1000 litres per day. Targeting customers above this level for the First Fix scheme is an attempt to engage customers in properties that are using over three times the national average usage. (342 litres per property per day, as calculated by the CRU (CRU/17/339)).
- The average daily usage of the property and the expected daily usage of 125 litres per person per
 day were included on the notification letter. This informs the customer of the quantity of excess
 usage at their property and will encourage the customer to engage with us in order to arrange a
 leak investigation.
- In order to improve customer engagement, Irish Water has revised the previous CFA notification issued during the metering programme by the inclusion of additional information on the latest CFA letters, to make the communication as informative as possible to customers.

Waiver Return Process

Under the metering programme, waivers were posted to customers that qualified for a leak repair following the investigation. The customer was required to sign the waiver and post it back to Irish Water. It was found that there was a delay in customers returning the waivers and in some cases the waiver was not returned.

Under the leakage reduction programme this process has been amended to increase the return of the signed waivers;

Upon completion of the Leak Investigation, the crew issue the waiver to the customer and answer
any questions the customer may have. If the customer is willing to sign the waiver at the time, the



crew will return the signed waiver to Irish Water and a repair can be scheduled. They will also leave a copy of the waiver with the customer for their own reference.

If the customer is not willing to sign the waiver at this time, the crew will issue the waiver and a
pre-paid envelope to the customer in the hope the customer will sign the waiver and post it back to
Irish Water.

Irish Water is also encouraging our contractors to be pro-active and contact customers that have received a first fix letter but have not engaged with the scheme.

5. First Fix Update

In the period of the transition of the First Fix Leak Repair scheme from the Metering Programme to the LRP, there was a temporary postponement on the issuance of CFA notifications from the end of Q4 2016 until the end of Q2 2017. This was to facilitate procurement competition for the LRP. During this period, Irish Water and its interim contractor continued to engage with Customers reporting possible leaks and carried out investigations to assess qualification and repair. Irish Water recommenced the issuance of CFA notifications under the LRP upon contractor mobilisation in August 2017.

In Q2, letters were sent to customers that appeared on the CFA list starting with the highest users. It was found that 3,477 properties that were using more than 5,000 litres per day based on meter readings and were accountable for nearly 41 million litres of Unaccounted for Water (53%).

Targeting these users first will result in greater savings from fewer repairs and reduce the UFW more effectively. The remaining 60,129 properties using less than 5,000 litres per day accounted for over 36 million litres of Unaccounted for Water (47%). The following table is calculated using information from the CFA list and figures calculated by the CRU (CRU/17/339) suggesting an average household consumes 342 litres of water per day.

Item	QTY of Leaks	Average usage (Litres)	Total Usage (Litres)	Expected Usage (Litres)	UFW (Litres)	% of UFW
>5 000 Litres	3,477	12,132	42,182,420	1,189,134	40,850,729	53%
Up to 5 000 Litres	60,129	985	59,240,773	20,564,118	36,211,366	47%
Total	63,606	1,595	101,423,193	21,753,252	77,062,095	100%

Table 1: Unaccounted for Water (UFW) summary Q2 2018

6. Reporting on the scheme

In April 2015, the CRU consulted on Irish Water's proposed First Fix Leak Repair Scheme for Domestic Water Customers and received eight responses. The CRU's decision on the policy, issued on 5 August 2015, was based on a review of the eight submissions received during the consultation period. Among its recommendations, the CRU expects Irish Water to strongly promote the scheme in order to increase customer awareness of the scheme and to encourage customers to engage with Irish Water on the scheme.



The CRU is monitoring the ongoing implementation of the scheme to ensure that the costs allowed are efficiently incurred and that benefits are achieved for customers. In line with the CRU Decision CER/15/178, Irish Water is to report on a quarterly basis on the progress of the First Fix Leak Repair scheme, the following section outlines the progress of the scheme to the end of Q2 2018.

7. Quarterly Summary

Constant Flow Advice Letters, Customer Response Rates and Engagement Levels

The total number of constant flow advice letters issued at the end of Q2 2018 was 16,456.

A total of 7,172 customers have engaged with the scheme in Q2 2018, representing 44% of the 16,456 constant flow advice letters issued. This number is made up of the following;

6,044 Customers requesting a free leak investigation survey

1,128 Customer repairs completed from data collected from the meter

• Leak Investigations

A total of 6,044 investigations were requested, which include repeat visits where customers installed an Internal Stop Valve (ISV) after an initial leak investigation visit.

Irish Water contacts customers within 10 business days to arrange a convenient time for an appointment to carry out the free leak investigation at a property. A total of 4,646 leak investigations had been undertaken in Q2 2018. The remaining customers that had requested a leak investigation in Q2 2018 either had appointments scheduled or were in the process of having appointments scheduled.

From the 4,646 completed leak investigations, 563 leaks on external supply pipes were identified. Irish Water has offered these customers with leaks on their external supply pipe a free leak repair under the scheme. The remaining 4083 non-qualifying leaks are broken down as follows:

- 1) A total of 1,054 properties surveyed did not have an operational Internal Stop Valve (ISV) and the survey could not be progressed, or required a further point of entry dig to establish the leak location. In many of these cases, the ISV was present but not operational. Customers are advised of the need to have a working ISV installed in order for the leak investigation to be completed.
- 2) In addition, a total of 113 properties have been identified through the First Fix process where the property does not qualify or the survey could not progress as it is served through a shared or backyard service.



- 3) The investigations identified 1,345 internal plumbing and other issues, which come under the remit of the home owner. As with all internal repair and maintenance in a customer's home, if a leak is confirmed internal to the house then it should be repaired by the homeowner.
- 4) The remaining 1,571 properties were identified as having leaks either on the public side, inaccessible leaks or otherwise out of the scope of the First Fix for Free Scheme

Leak Repairs

Customers are asked to review the terms and conditions of the leak repair offer and sign the offer documentation after which Irish Water will contact the customer to schedule the leak repair at a suitable time. On receipt of the documentation, Irish Water contacts customers within 10 working days to arrange a convenient time for an appointment to carry out the free leak repair at a property.

During Q2 2018 Irish Water had completed 982 free leak repairs under the First Fix Leak Repair scheme. The remaining 617 customers to whom Irish Water offered a free leak repair either had a repair scheduled or had yet to accept the leak repair offer.

Customer Repairs

From the data collected through meter reading we know that 1,128 customers have repaired leaks on their property themselves after receiving a constant flow advice letter. Irish Water would like to thank all customers who repaired leaks on their property. These repairs have made a significant contribution to national water conservation.

Water Savings

The issuance of constant flow advice letters has targeted the largest leaks first and the result of this can be seen from the estimated incremental savings of 4.40 million litres of water per day achieved in Q2 2018 from contractor repairs and a further 2.91 million litres from customer repairs.



2018	Irish Water First Fix Repair		Customer Repairs		2018 Total: Q1-Q4	
Quarter	Repairs #	Savings (ML/Day)	Repairs #	Savings (ML/Day)	Total Repairs	Total Savings (ML/Day)
1	671	3.61	858	2.36	1,529	5.97
2	982	4.40	1,128	2.91	2,110	7.31
3						
4						
Total	1,653	8.01	1,986	5.27	3,639	13.28

Table 2: Estimated water savings from the First Fix Scheme and Customer Repairs for Q1-Q4 2018.

Since commencement of the First Fix Scheme, total cumulative water savings are estimated at 128.88 ML per day. A cumulative estimated total of 61.48 million litres per day has been saved through First Fix repairs and a further estimated 67.40 million litres from customer repairs. Savings are calculated from a comparison of meter data collected prior to and after the repair work being undertaken. For customer repairs, the constant flow alert is no longer active and the meter data shows a supporting drop in water usage over the next two read periods. Finally we exclude those with less than 1000l/d as it is suspected that below this level usage has been reduced rather than an actual customer leak repair.

8. Project Expenditure

The project expenditure is reported quarterly in arrears. The cumulative total expenditure up to the end of Q1 2018 (end of March 2018) is €25,715,036 consisting of €12,143,189 for leak investigations, €9,767,706 for repairs and €3,804,141 for additional costs.

9. Next Steps

Irish Water will continue to implement the First Fix Leak Repair scheme through the LRP and will issue the next quarterly report, for Q3 2018, to the CRU in Q2 2019.



Table 1: Project Summary

	N. 1. 6		02 2018				
1	Number of Continuous Flow	Total	Q2 2018	-			
1	Alarms Detected	lotai	63,606				
		Period	Q2 2018	Cumulative FF Scheme Total			
		Region	Q2 2018	cumulative 11 Selicine Total			
	Number of Customer Notifications Issued	North	998				
		North West	2,337				
		South East	1,959				
2		South West	2,721				
		Dublin	2,168	152,581			
		North East	2,372				
		Midlands	1,675				
		Midwest	2,226				
		Grand Total	16,456				
	A total number of 16,4 send letters in Q3 2018		advice letters were issued in Q2.	Irish Water will continue to			
		Period	Q2 2018	Cumulative FF Scheme Total			
	Customer Responses requesting a Free Leak Investigation	Region	Q2 2018	Cumulative FF Scheme Total			
		North	423				
		North West	996				
		South East	541				
3		South West	828				
		Dublin	1,391	54,937			
		North East	723				
		Midlands	501				
		Midwest	641				
		Grand Total	6,044				
	6,044 customers requested a First Fix Free Leak Investigation						
	Leak Investigations Completed		Period	Q2 2018	Cumulative FF Scheme Total		
		Region	Q2 2010	Samalative II Scheme Islan			
		North	284				
		North West	787				
4		South East	396				
		South West	665				
		Dublin	1,017	53,431			
		North East	578				
		Midlands	562				
		Midwest	357				
		Grand Total	4,646				
	4,646 Leak Investigatio	ns were carried o	ut in Q2 by WNP contractors.				



		Period	02 2042	C Lut FF Cilo Tutil
		Region	Q2 2018	Cumulative FF Scheme Tota
		North	69	
		North West	200	
		South East	97	
4a	Leak Repairs Created	South West	195	
		Dublin	477	14,067
		North East	175	
		Midlands	276	
		Midwest	110	
		Grand Total	1,599	
	1,599 Leak Repairs wer	e created in Q2 2	018	
		Period	O2 2019	Cumulative FF Scheme Tota
		Region	Q2 2018	Cumulative FF Scheme 10ta
		North	39	
		North West	103	
	Look Donoine	South East	90	
5	Leak Repairs Completed	South West	223	
		Dublin	182	10,471
		North East	32	
		Midlands	218	
		Midwest	95	
		Grand Total	982	
	982 confirmed Leak Re	pairs carried out i	n Q2	
		Period	Q2 2018	Cumulative FF Scheme Tota
	Estimated Water Savings from First Fix Repairs (Litres/day)	Region	Q2 2018	Cumulative II Scheme Tota
		North	224,488	
		North West	494,836	
		South East	478,846	
6		South West	1,114,013	
		Dublin	906,640	61.48 ML
		North East	223,703	
		Midlands	701,998	
			•	
		Midwest	254,005	

It is estimated that 4.40ML of water was saved in Q2 as a result of repairs carried out by the contractor This brings the total incremental Water Savings to 61.48 ML from contractor repairs and an overall saving of 128.88 ML per day.



		Period	03 3040	Commission FF Calcana Tata	
		Region	Q2 2018	Cumulative FF Scheme Tota	
		North	88		
		North West	172		
	C alama Bassin	South East	166		
7	Customer Repairs Completed	South West	180		
	Completed	Dublin	110	40,618	
		North East	186		
		Midlands	46		
		Midwest	180		
		Grand Total	1,128		
		·	carried out by the customer after	er receiving a First Fix Free lette	
	from Irish Water. 1,128	·	red leaks in Q2.		
		Period	Q2 2018	Cumulative FF Scheme Tota	
		Region			
		North	248,660		
		North West	444,021		
_	Estimated Savings	South East	463,248	-	
8	from Customer	South West	485,596		
	Repairs (Litres/day)	Dublin	252,523	67.40	
		North East	528,380		
		Midlands	84,706		
		Midwest	400,353		
		Grand Total	2,907,487		
			saved in Q2 as a result of Repa avings to 67.40ML from custom	•	
		Period	03 3010	Comparison FF Calculation Tab	
		Region	Q2 2018	Cumulative FF Scheme Total	
		North	49		
		North West	128		
9	Known Properties Without an Operational ISV	South East	19		
		South West	65		
		Dublin	157	10,608	
		North East	80		
		Midlands	32		
		Midwest	2		
		Grand Total	532		
	A total of 532 propertion progressed.	Midwest Grand Total	2	ak Investigation could not be	



	Number of Non- Qualifying Properties Served Through a Shared or Backyard Pipe	Total	Q2 2018	Cumulative FF Scheme Total	
10			113	935	
	113 properties were identified as not qualifying for the scheme as they are served through a shared supply or backyard supply.				
	Counties in Each Region	North	Donegal, Cavan, Monaghan, Leitrim		
		North West	Galway, Galway City, Mayo, Sligo, Roscommon		
		South East	Carlow, Waterford, Waterford City, Kilkenny, Wexford		
11		South West	Cork, Cork City, Kerry		
11		Dublin	Dublin City, South Dublin, Dun Laoghaire Rathdown, Fingal		
		North East	Longford, Louth, Meath, Westmeath		
		Midlands	Kildare, Offaly, Laois, Wicklow		
		Midwest	Limerick, Clare, Tipperary		

Note: All cumulative totals outlined in table 3 are for the First Fix Scheme from commencement to the end of Q2 2018.

Note: Meter read data is used to confirm that a customer repair has been carried out. Number of customer repairs and estimated savings will be included in the report once two confirmed meter readings are collected after the repair date. As such, the number of customer repairs noted above for each month is expected to increase in the next report as more confirmed readings are collected.
